

Capital Project Update

Date: May 25, 2018
From: Frank Ferraro
Subject: May 25, 2018 Update

The Capital Project will officially begin next week with the start of abatement in the elementary boiler room and the demolition of the red storage facility next to the basketball courts adjacent to the High School parking lot. A map showing the abatement schedule and phasing plan is attached.


We have contracted with Arnoff Movers and next week they will be providing detailed plans of what needs to take place to move classrooms in preparation for the summer construction work. I will then meet with principals and faculty to provide this specific information. We will also meet with our facilities staff to coordinate moving and construction schedules.

Contracts for the major trades have been awarded and approved by the Board of Education. We are planning to list this information on the District website under the *Capital Project Quick Link*. All information, including construction meeting agendas and notes will be available on the site.

Abatement Plan Summer 2018

EXHIBIT-C

Note - Storage Building Abatement
5/28/2018 - 6/22/2018

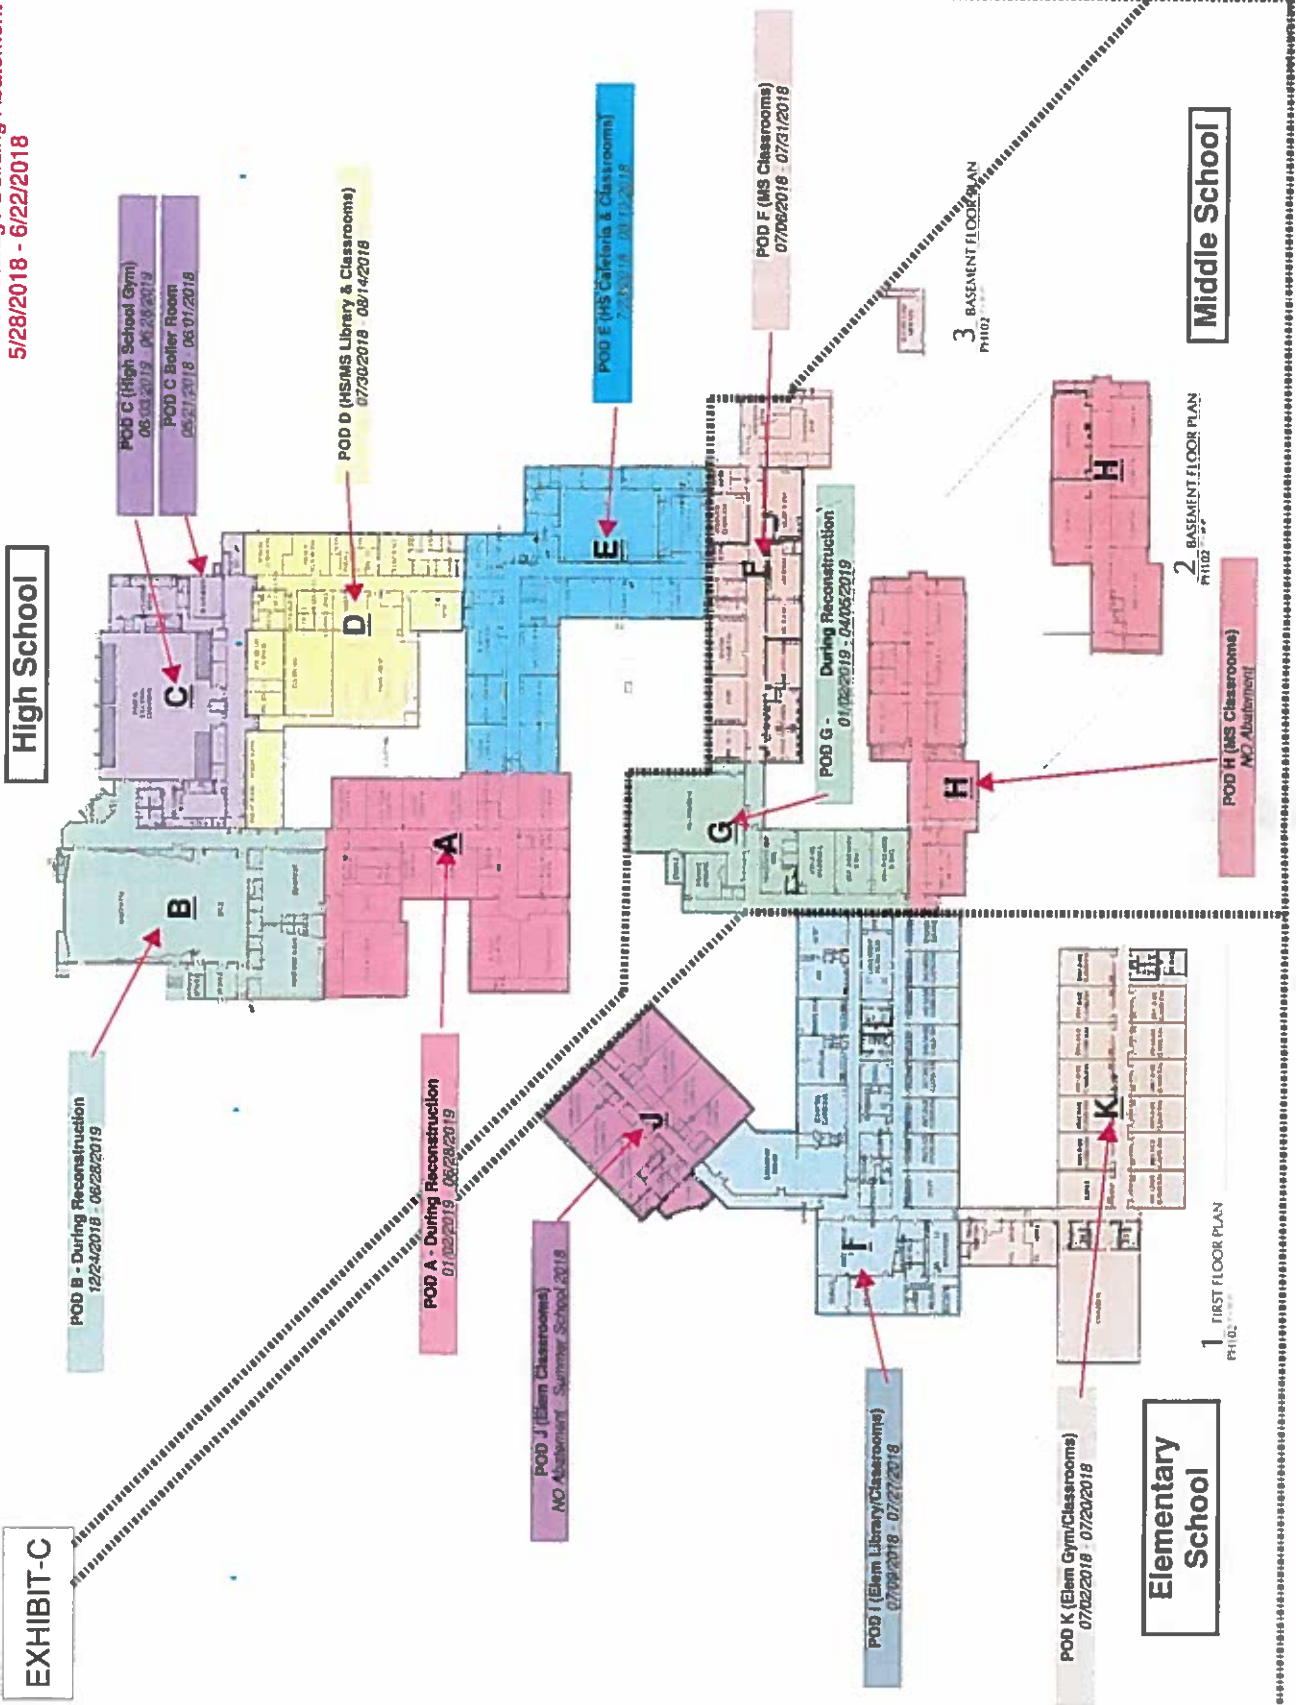

GALWAY CENTRAL SCHOOL DISTRICT
K-12 FACILITY
2016 CAPITAL PROJECT

| | |
|-------|------------------------------|
| | ABATEMENT PHASING PLAN |
| | DRWT 2.26.18 REV 0 |
| PH102 | K-12 |
| PH102 | PH102 |

Phasing Plan Summer 2018/2019

EXHIBIT-C


| | | |
|------------------------------------|-------------------------|-----------|
| POD K (Elem Gym Classrooms) | 08/22/2018 - 12/22/2018 | 1st Shift |
| POD I (Nathan Hale-Purcell) | 08/28/2018 - 08/17/2018 | 1st Shift |
| POD B (Auditorium/Music) | 07/02/2018 - 07/20/2018 | 1st Shift |
| POD J (Addition) | 08/20/2018 - 12/21/2018 | 1st Shift |
| POD I (Elem Library Classrooms) | 12/24/2018 - 08/26/2019 | 1st Shift |
| POD A (High School Classrooms) | 07/02/2019 - 08/29/2019 | 2nd Shift |
| POD G (MS Gym Classrooms) | 07/02/2019 - 04/05/2019 | 2nd Shift |
| POD H (MS Classrooms) | 07/02/2019 - 04/05/2019 | 2nd Shift |
| POD D (HS/MS Library & Classrooms) | 04/06/2019 - 08/15/2019 | 2nd Shift |
| POD E (MS Cafeteria & Classrooms) | 07/15/2019 - 04/13/2019 | 2nd Shift |
| POD F (MS Classrooms) | 04/15/2019 - 08/13/2019 | 1st Shift |
| POD C (High School Gym) | 08/03/2019 - 08/23/2019 | 1st Shift |
| POD J (Elem Classrooms) | 08/24/2019 - 8/30/2019 | 1st Shift |

NOTES

- 1) Storage Building Abatement 5/28/2018 - 6/22/2018
- 2) Summer School 7/09/18 - 8/02/2018
Elementary Classes in POD J
Junior/Senior High in POD H

High School

Middle School

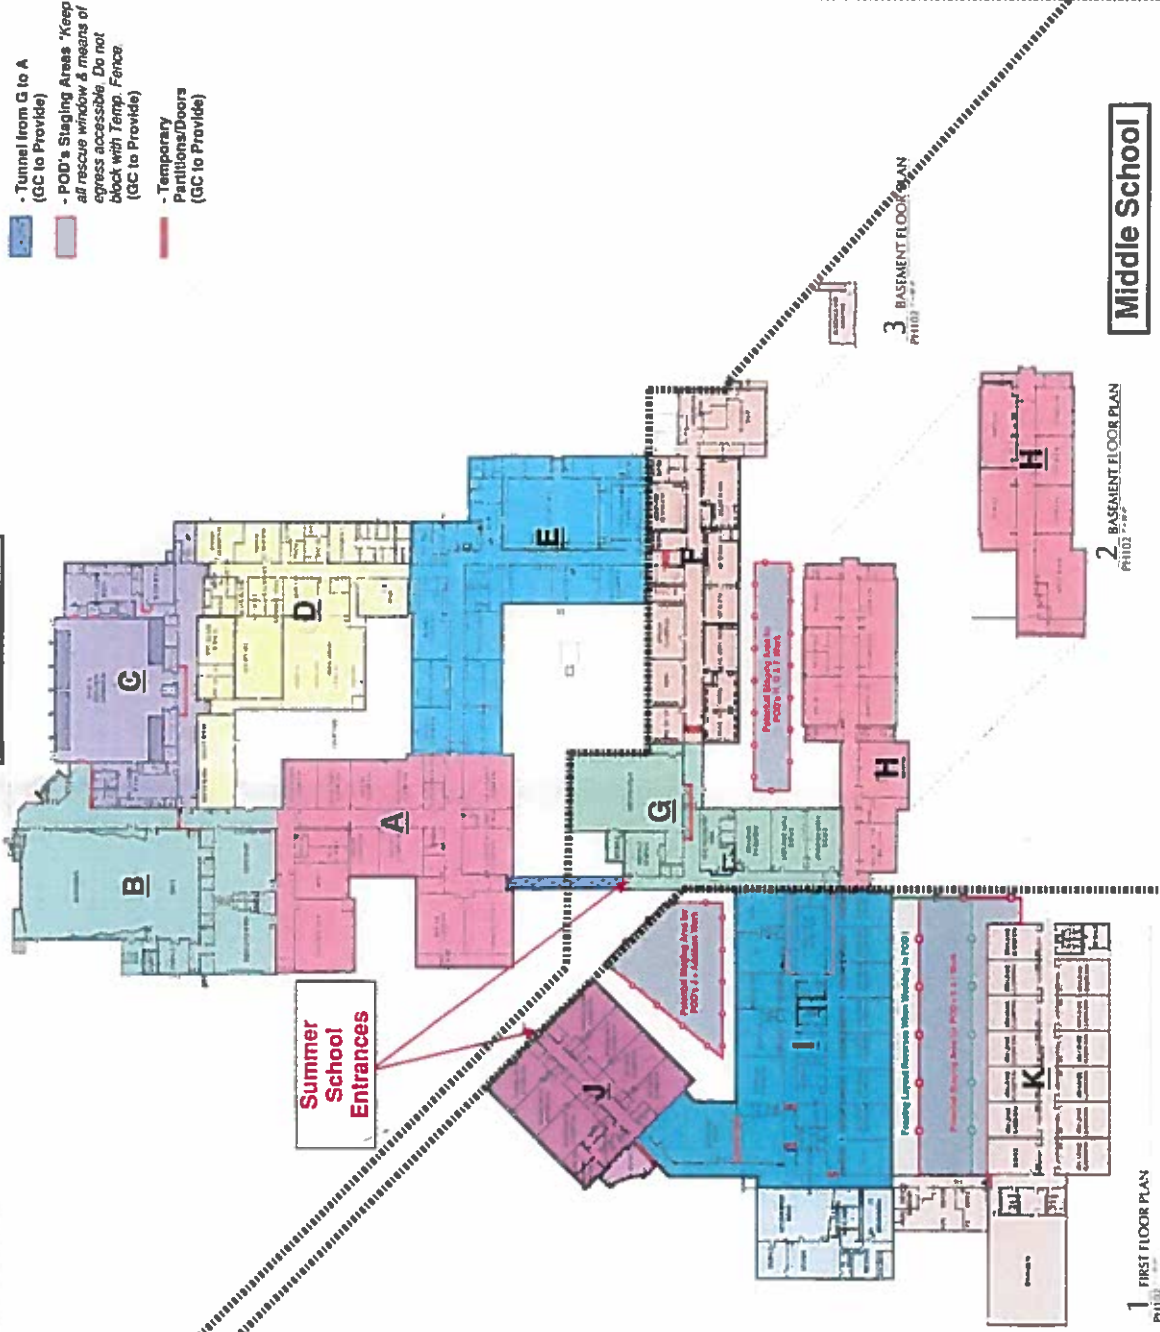

GALWAY CENTRAL SCHOOL DISTRICT
2016 CAPITAL PROJECT




| | |
|-------------------|--|
| Project No. | |
| Client | |
| Architect | |
| Engineer | |
| Interior Designer | |
| Contractor | |
| Phase | |
| Date | |

TURNER
1000 BROADWAY
SUITE 2000
NEW YORK, NY 10018
PH: 212.904.6500
WWW.TURNERINC.COM

Site Phasing Plan Summer 2018/2019

EXHIBIT-I

| |
|--|
| Elementary Site Reconstruction 06/24/2019 - 08/30/2019 |
| HS/MS Bus Loop/Main Entrance (Binder/Stripe ONLY) 08/25/2018 - 09/17/2018 |
| HS/MS Bus Loop/Main Entrance (Finish) 07/01/2019 - 08/30/2019 |
| Student Parking Lot 08/25/2018 - 09/17/2018 |
| Phase I - Tennis Courts Stabilization (Temp. Striping) 06/25/2018 - 07/01/2019 |
| Phase I - Utility Road & Student Parking Prep. (Stabilize & Binder/Stripe) 6/25/18 - 9/17/2018 |
| Phase II - Tennis Courts/Utility Reconstruction/Student Parking Lot (Finish) 07/01/2019 - 08/30/2019 |
| OWNER OCCUPIED Duration of Project |

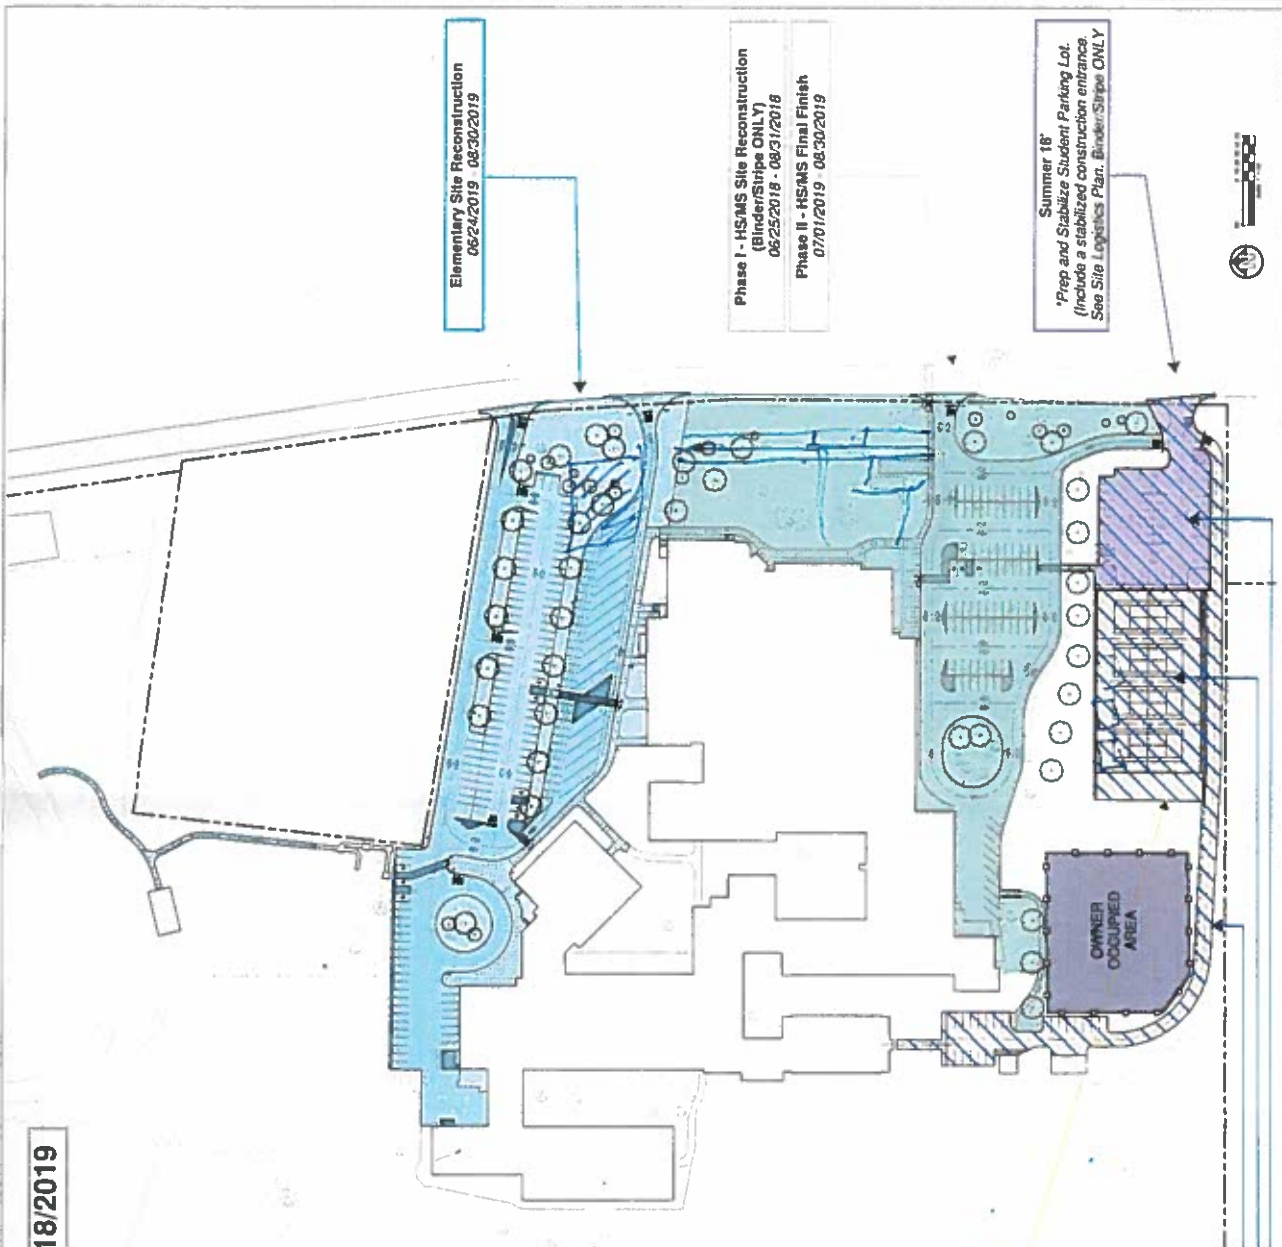

Elementary Site Reconstruction
06/24/2019 - 08/30/2019

Phase I - HS/MS Site Reconstruction
(Binder/Stripe ONLY)
06/25/2018 - 09/17/2018
Phase II - HS/MS Final Finish
07/01/2019 - 08/30/2019

Summer 18
*Prep and Stabilize Student Parking Lot.
(Include a stabilized construction entrance.
See Site Logistics Plan, Binder/Stripe ONLY

Phase I - Prep, Tennis Courts
6/25/18 - 7/01/2019
*Prep and Stabilize for Contractor law down
area

Phase I - Utility Road & Student Parking
Prep. (Stabilize & Binder/Stripe)
6/25/18 - 9/17/2018

Phase II - Tennis Courts, Utility Road &
Student Parking Finish Work
7/01/19 - 8/30/2019
*Compact and Finish all work in this area.
